

CURRENT ACTIVITIES

- Scaffolding nearing completion on the West elevation.
- Masonry complete on the Northeast elevation and ongoing on the Southwest elevation.
- Basement ceiling grid continuing in hallways, bathroom tile ongoing.
- 1st Floor Glass installation in progress at South and Primer and Paint ongoing at North.
- 2nd Floor drywall taping and aluminum frame install on going.
- 3rd Floor Drywall ongoing at South and overhead MEP at the North.
- 4th Floor Framing nearing completion.

FUN FACT

In the upcoming week the building roofing will be completed, which will conclude nearly 35,000 square feet of installed roofing product. This is enough roofing to to cover 15-20 average sized homes.



[Click here for the LIVE WEBCAM](#)

Weekly Progress Photos

Bioscience Research Laboratories
University of Arizona + DPR Construction

Scaffolding on Northwest Building Elevation




Ceiling Grid in Basement Corridors



Masonry at West Elevation



Basement Bathroom Wall Tile

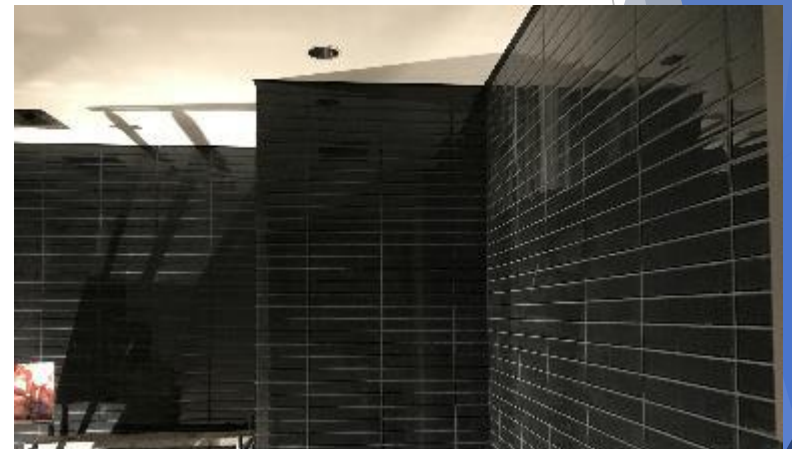

Weekly Progress Photos

Bioscience Research Laboratories
University of Arizona + DPR Construction

1st Floor 14' Tall Glass Installation



3rd Floor Overhead Rough-in and Drywall



2nd Floor Aluminum Glazing Frames



4th Floor Wall Framing at Perimeter Rooms

